



ENGINEER FAULT REPORT

Results from test JOB13071

Test date 08/09/2025

To:

90 Paul Street
London

EC2A 4NE


Site Address:

47 Richmond Road
Hackney
London

E8 3BF

The purpose of this report is to try and provide an easy-to-read explanation of any C1 or C2 faults that have been found during a test. It should be used as a reference guide only, with full details of any faults being on page 2 of the Electrical Installation Condition Report (EICR).

47 Richmond Road

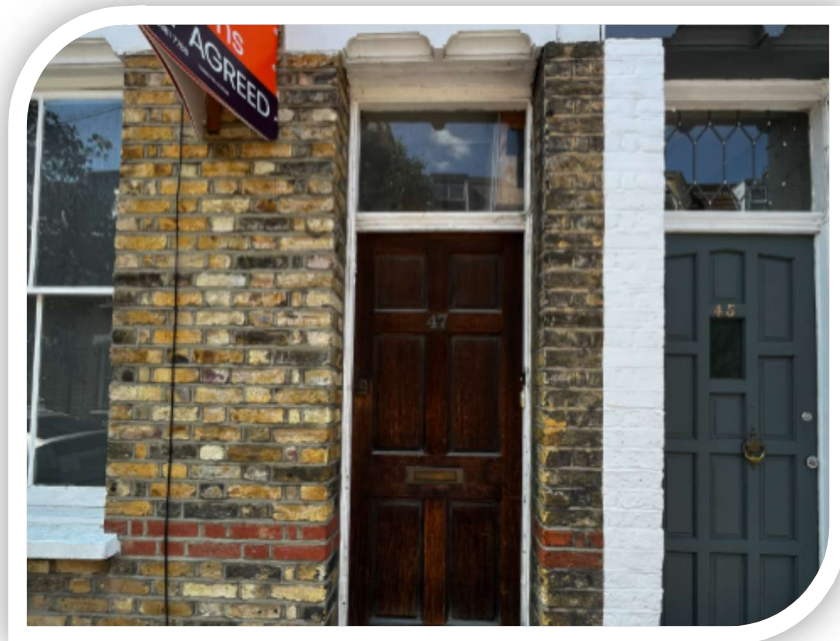



ENGINEER FAULT REPORT

FAULT REPORT

Water supply

C2 FAULT



FAULT DESCRIPTION

Water : Main equipotential earth bonding cable has been disconnected from the water supply pipework(A15).

WHAT DOES THIS MEAN?

There should be a green and yellow earth cable connected to the water supply pipe that runs back to the fuse board which is not connected.

WHAT NEEDS TO BE DONE?

Reconnect the existing earth bonding cable to the water supply pipe.

Rectified on site -

Fixed Onsite



FAULT DESCRIPTION

Rectified on site - no earth bond cable connected to the water supply pipework
(Water connection - Visual Inspection)

WHAT WAS DONE?

Reconnected the earth bonding cable to water pipe and confirmed is connected



electrical testing inspection

ENGINEER FAULT REPORT

Signature

A handwritten signature in black ink, appearing to be 'Jr'.

Tenant NOT present at time of test.

02/03/2026 15:47
